


		Nombre	Duracion	Inicio	Terminado	Predecesores
1	✓	1. Arranque del reto	1 day	5/3/26, 8:00	5/3/26, 17:00	
2	✓	2. Actividad de arranque del reto	4 days	5/3/26, 8:00	10/3/26, 17:00	
3	✓	2.1 División de responsabilidades	1 day	5/3/26, 8:00	5/3/26, 17:00	
4	✓	2.2 Desarrollo de responsabilidades	3 days	6/3/26, 8:00	10/3/26, 17:00	3
5	✓	3. Q&A con Socio Formador	2 days	11/3/26, 8:00	12/3/26, 17:00	
6	✓	3.1 Preparación de preguntas	1 day	11/3/26, 8:00	11/3/26, 17:00	4
7	✓	3.2 Sesión de Q&A	1 day	12/3/26, 8:00	12/3/26, 17:00	6
8	✓	4. Desarrollo de la primera aplicación (fase 1)	60 days	13/3/26, 8:00	4/6/26, 17:00	
9	✓	4.1 Lluvia de ideas	1 day	13/3/26, 8:00	13/3/26, 17:00	7
10	✓	4.2 División de responsabilidades	1 day	16/3/26, 8:00	16/3/26, 17:00	9
11	✓	4.3 Reunión de ideación inicial	1 day	17/3/26, 8:00	17/3/26, 17:00	10
12	✓	4.4 Desarrollo de responsabilidades	4 days	18/3/26, 8:00	23/3/26, 17:00	11
13	✓	5. Sesiones de revisión de reto con Profesor	1 day	24/3/26, 8:00	24/3/26, 17:00	
14	✓	5.1 Sesión 1 de revisión	1 day	24/3/26, 8:00	24/3/26, 17:00	12
15	✓	5.2 Correcciones Sesión 1	3 days	25/3/26, 8:00	27/3/26, 17:00	
16	✓	5.2.1 Investigación de Softwares permitidos	1 day	25/3/26, 8:00	25/3/26, 17:00	14
17	✓	5.2.2 Elaboración de diagrama de desarrollo de aplicación	1 day	26/3/26, 8:00	26/3/26, 17:00	16
18	✓	5.2.2 Sesión 2 de revisión	1 day	27/3/26, 8:00	27/3/26, 17:00	17
19	✓	5.3 Correcciones Sesión 2	7 days	30/3/26, 8:00	7/4/26, 17:00	
20	 ✓	5.3.1 Corregir marco teórico	1 day	30/3/26, 8:00	30/3/26, 17:00	18
21	✓	5.4.2 Corregir diagrama de desarrollo de aplicación	2 days	31/3/26, 8:00	1/4/26, 17:00	20
22	✓	SEMANA SANTA	2 days	2/4/26, 8:00	3/4/26, 17:00	21
23	✓	5.3.3 Revisión antes de sesión con profesor	1 day	6/4/26, 8:00	6/4/26, 17:00	22
24	✓	5.3.4 Sesión 3 de revisión	1 day	7/4/26, 8:00	7/4/26, 17:00	23
25	✓	5.4 Correcciones Sesión 3	3 days	8/4/26, 8:00	10/4/26, 17:00	
26	✓	Realizar ejemplos de código con base en diagramas	1 day	8/4/26, 8:00	8/4/26, 17:00	24
27	✓	Definir cómo agregar nuevos usuarios	1 day	9/4/26, 8:00	9/4/26, 17:00	26
28	✓	5.4.3 Sesión 4	1 day	10/4/26, 8:00	10/4/26, 17:00	27
29	✓	5.5 Correcciones Sesión 4	2 days	13/4/26, 8:00	14/4/26, 17:00	
30		Definir generación de certificados	0 days	13/4/26, 8:00	13/4/26, 8:00	28
31	✓	Definir permisos del administrador	1 day	13/4/26, 8:00	13/4/26, 17:00	30
32	✓	5.5.3 Sesión 5	1 day	14/4/26, 8:00	14/4/26, 17:00	31
33	✓	5.6 Correcciones Sesión 5	3 days	15/4/26, 8:00	17/4/26, 17:00	
34	✓	Incorporar capturas de aplicación al documento	1 day	15/4/26, 8:00	15/4/26, 17:00	32

[illegible]

		Nombre	Duracion	Inicio	Terminado	Predecesores
35	✓	Definir repartición de certificados	1 day	16/4/26, 8:00	16/4/26, 17:00	34
36	✓	5.6.3 Sesión 6	1 day	17/4/26, 8:00	17/4/26, 17:00	35
37	✓	5.7 Correcciones Sesión 6	2 days	20/4/26, 8:00	21/4/26, 17:00	
38	✓	Completar tabla de pruebas	1 day	20/4/26, 8:00	20/4/26, 17:00	36
39		Reforzar avances en marco teórico	0 days	20/4/26, 17:00	20/4/26, 17:00	38
40	✓	5.7.3 Sesión 7	1 day	21/4/26, 8:00	21/4/26, 17:00	39
41	✓	5.8 Correcciones Sesión 7	3 days	22/4/26, 8:00	24/4/26, 17:00	
42	✓	Definir niveles de autorización	1 day	22/4/26, 8:00	22/4/26, 17:00	40
43	✓	Asegurar de que el certificado sea de uno por persona	1 day	23/4/26, 8:00	23/4/26, 17:00	42
44	✓	5.8.3 Sesión 8	1 day	24/4/26, 8:00	24/4/26, 17:00	43
45	✓	5.9 Correcciones Sesión 8	2 days	27/4/26, 8:00	28/4/26, 17:00	
46		Poner casos principales en el reporte técnico	0 days	27/4/26, 8:00	27/4/26, 8:00	44
47	✓	Completar el reporte ejecutivo con objetivos	1 day	27/4/26, 8:00	27/4/26, 17:00	46
48	✓	5.9.3 Sesión 9	1 day	28/4/26, 8:00	28/4/26, 17:00	47
49	✓	5.10 Correcciones Sesión 9	13 days	29/4/26, 8:00	15/5/26, 17:00	
50	✓	Corregir tablas en la documentación	3 days	29/4/26, 8:00	1/5/26, 17:00	48
51	✓	Preparación de la demo	9 days	4/5/26, 8:00	14/5/26, 17:00	50
52	✓	5.10.3 Sesión 10	1 day	15/5/26, 8:00	15/5/26, 17:00	51
53	✓	5.11 Correcciones Sesión 10	2 days	18/5/26, 8:00	19/5/26, 17:00	
54	✓	Dar de alta usuarios temporales	1 day	18/5/26, 8:00	18/5/26, 17:00	52
55		Preparar lista de usuarios y contraseñas para demo	0 days	18/5/26, 17:00	18/5/26, 17:00	54
56	✓	5.11.3 Sesión 11	1 day	19/5/26, 8:00	19/5/26, 17:00	55
57	✓	5.12 Correcciones Sesión 11	3 days	20/5/26, 8:00	22/5/26, 17:00	
58	✓	Agregar asignación de tareas por área	1 day	20/5/26, 8:00	20/5/26, 17:00	56
59	✓	Implementar derechos ARCO	1 day	21/5/26, 8:00	21/5/26, 17:00	58
60	✓	5.12.3 Sesión 12	1 day	22/5/26, 8:00	22/5/26, 17:00	59
61	✓	5.13 Correcciones Sesión 12	2 days	25/5/26, 8:00	26/5/26, 17:00	
62		Perfeccionar proceso de solicitud ARCO	0 days	25/5/26, 8:00	25/5/26, 8:00	60
63	✓	Revisar y confirmar CRUD	1 day	25/5/26, 8:00	25/5/26, 17:00	62
64	✓	5.13.3 Sesión 13	1 day	26/5/26, 8:00	26/5/26, 17:00	63
65	✓	5.14 Correcciones Sesión 13	3 days	27/5/26, 8:00	29/5/26, 17:00	
66	✓	Cambiar paleta de color a la marca de Casa Monarca	1 day	27/5/26, 8:00	27/5/26, 17:00	64
67	✓	Implementar Aviso de Privacidad	1 day	28/5/26, 8:00	28/5/26, 17:00	66
68	✓	5.14.3 Sesión 14	1 day	29/5/26, 8:00	29/5/26, 17:00	67

[illegible]

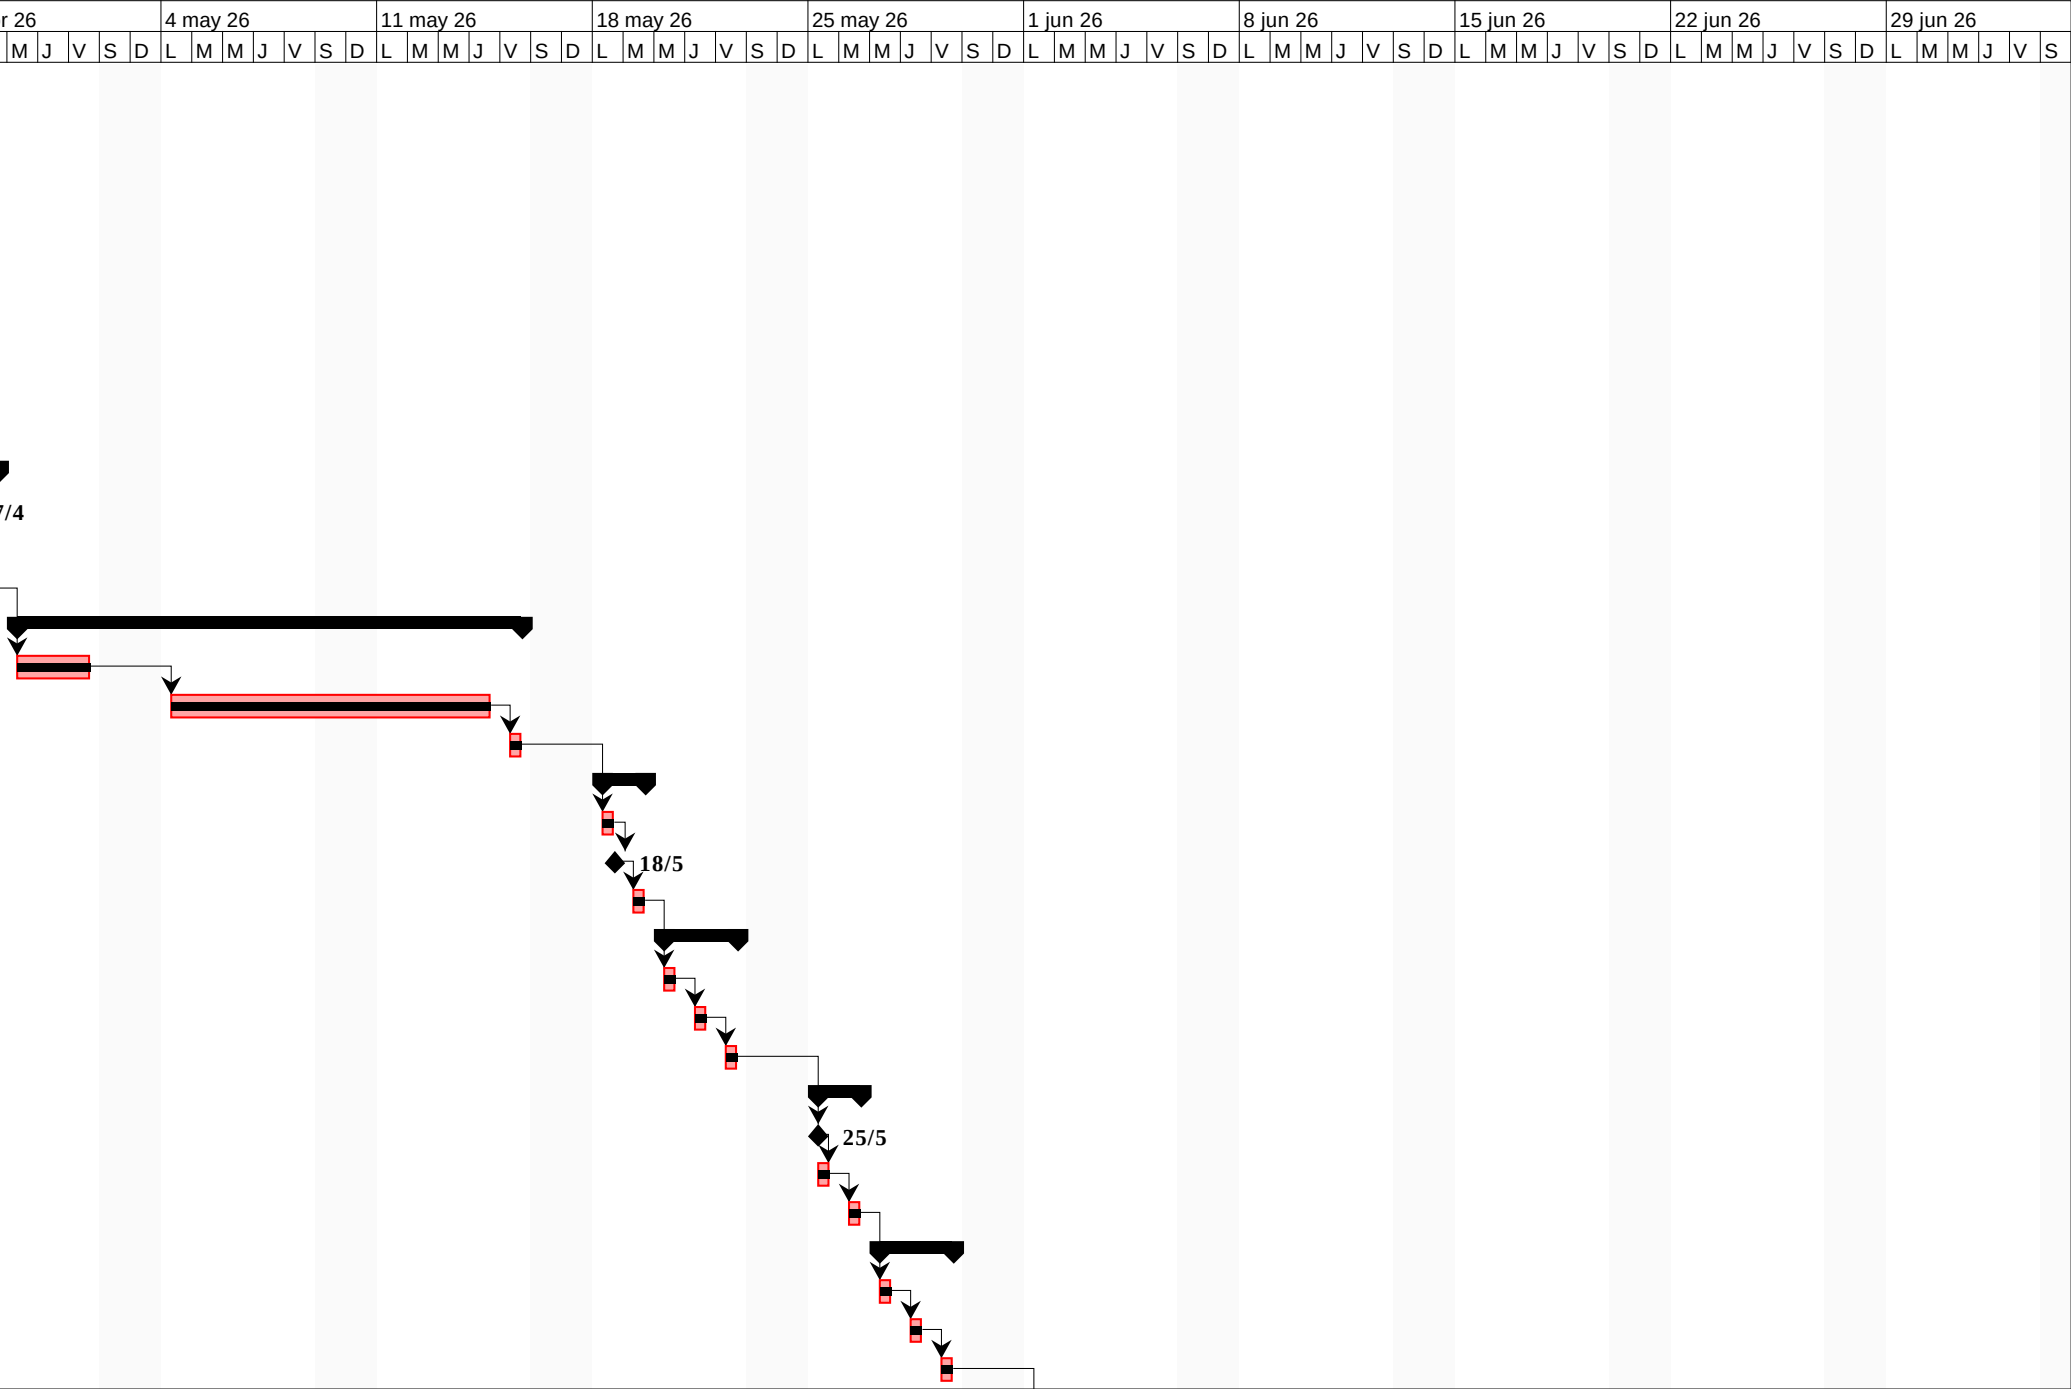

		Nombre	Duracion	Inicio	Terminado	Predecesores
69	✔	5.15 Correcciones Sesión 14	2 days	1/6/26, 8:00	2/6/26, 17:00	
70		Implementar términos y condiciones	0 days	1/6/26, 8:00	1/6/26, 8:00	68
71	✔	Perfeccionar línea de solicitud ARCO y revisar firmas	1 day	1/6/26, 8:00	1/6/26, 17:00	70
72	✔	5.15.3 Sesión 15	1 day	2/6/26, 8:00	2/6/26, 17:00	71
73	✔	5.16 Correcciones Sesión 15	1 day	3/6/26, 8:00	3/6/26, 17:00	
74	✔	Preparar demo	1 day	3/6/26, 8:00	3/6/26, 17:00	72
75	✔	6. Presentación final a Socio Formador	1 day	4/6/26, 8:00	4/6/26, 17:00	
76	✔	6.1 Presentación final	1 day	4/6/26, 8:00	4/6/26, 17:00	74

